PROJECT PLANNING PHASE
PRODUCT BACKLOG, SPRINT PLANNING, STORIES & ESTIMATION

Date	22 October 2026
Team ID	N/A — Individual Project
Project Name	ServiceNow-Based Employee Laptop Request Application
Maximum Marks	5 Marks

1. Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The backlog below organizes the Employee Laptop Request project into manageable work items. Story points are estimates of relative effort, not measured historical velocity. Sprint labels and durations are proposed planning values because exact sprint dates were not provided.

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint 1	Data Model & Fields	US-1	As an administrator, I can create a custom Laptop Request Form table with fields for employee, request type, reason, status, approver and request number.	3	High	Individual
Sprint 1	Data Model & Fields	US-2	As an administrator, I can configure request-number generation and field settings so each request can be identified and maintained consistently.	2	High	Individual
Sprint 1	Request Submission	US-3	As an employee, I can choose a request type (Basic or Advance) and enter a reason so my laptop need is described consistently.	3	High	Individual
Sprint 1	Request Submission	US-4	As an employee, I can open the Laptop Request Record Producer from the Service Portal and submit the form to create a record in the custom table.	3	High	Individual
Sprint 2	Validation & Policy	US-5	As a project owner, I can configure a business rule so an employee cannot submit more than one laptop request per year.	3	High	Individual
Sprint 2	Workflow	US-6	As an IT manager, I can approve or reject a request through a Flow Designer approval flow, and the status updates automatically.	5	High	Individual
Sprint 2	Security	US-7	As an administrator, I can create the roles it_manager and it_employee and the groups IT Managers and IT Employees, and assign users to them.	2	High	Individual
Sprint 2	Security	US-8	As an administrator, I can configure ACLs so managers have view-only access and IT employees can create and manage requests.	3	High	Individual
Sprint 3	Testing & Validation	US-9	As a project owner, I can test submission, the one-request-per-year rule, approval and role access, and confirm each works as expected.	3	High	Individual
Sprint 3	Deployment	US-10	As a developer, I can preview and commit the Update Set, resolve conflicts, and export it as XML for another instance.	2	Medium	Individual
Sprint 3	Documentation	US-11	As a project owner, I can prepare the final documentation and presentation that summarize the solution and its results.	3	Medium	Individual

2. Project Tracker, Velocity & Burndown Chart (4 Marks)

The sprint tracker below is a planning example, not a record of actual sprint performance. Update the completed story points and release dates with actual values if your submission requires them.


Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (Planned End)	Sprint Release Date (Actual)
Sprint 1	11	6 days	Proposed Day 1	Proposed Day 6	11 (target)	Not recorded
Sprint 2	13	6 days	Proposed Day 7	Proposed Day 12	13 (target)	Not recorded
Sprint 3	8	6 days	Proposed Day 13	Proposed Day 18	8 (target)	Not recorded

Velocity

Average velocity is story points divided by sprint duration. Planned target velocity for this project: Sprint 1 = 11 ÷ 6 ≈ 1.83, Sprint 2 = 13 ÷ 6 ≈ 2.17, Sprint 3 = 8 ÷ 6 ≈ 1.33 story points per day. Overall: 32 ÷ 18 ≈ 1.78 story points per day. These are planned values; actual velocity cannot be calculated reliably without actual sprint duration and completed-point data.

Burndown Chart

A burndown chart shows remaining work over time. The chart below is illustrative only and assumes 32 points of work reaching zero by project day 18; add actual daily remaining-work values when you have them.

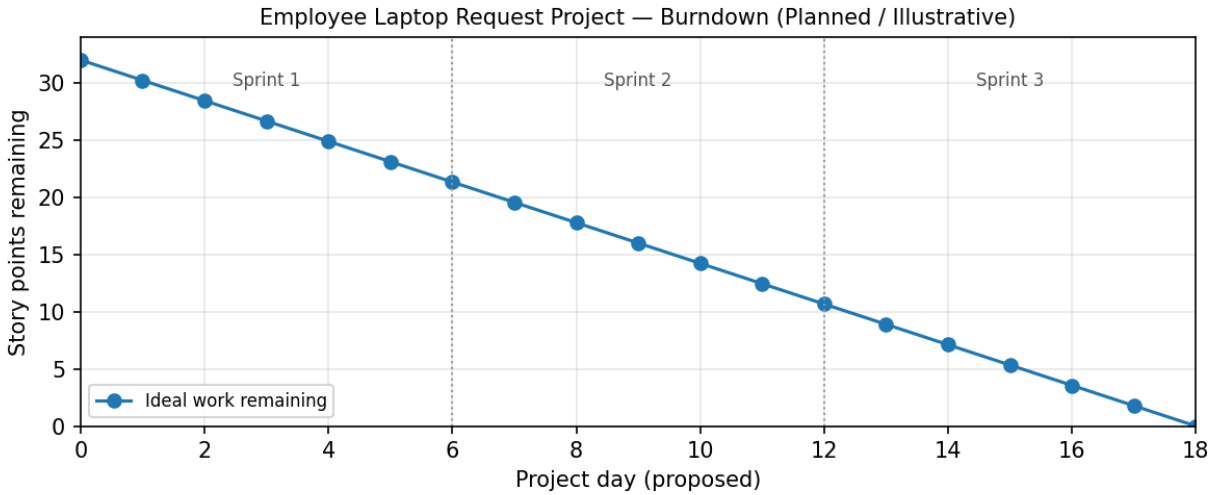

References

https://www.atlassian.com/agile/project-management
https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software
https://www.atlassian.com/agile/tutorials/epics
https://www.atlassian.com/agile/tutorials/sprints
https://www.atlassian.com/agile/project-management/estimation
https://www.atlassian.com/agile/tutorials/burndown-charts
https://www.visual-paradigm.com/scrum/scrum-burndown-chart/
